




The Sherman School - Construction Schedule
Data Date: 01-Jun-26



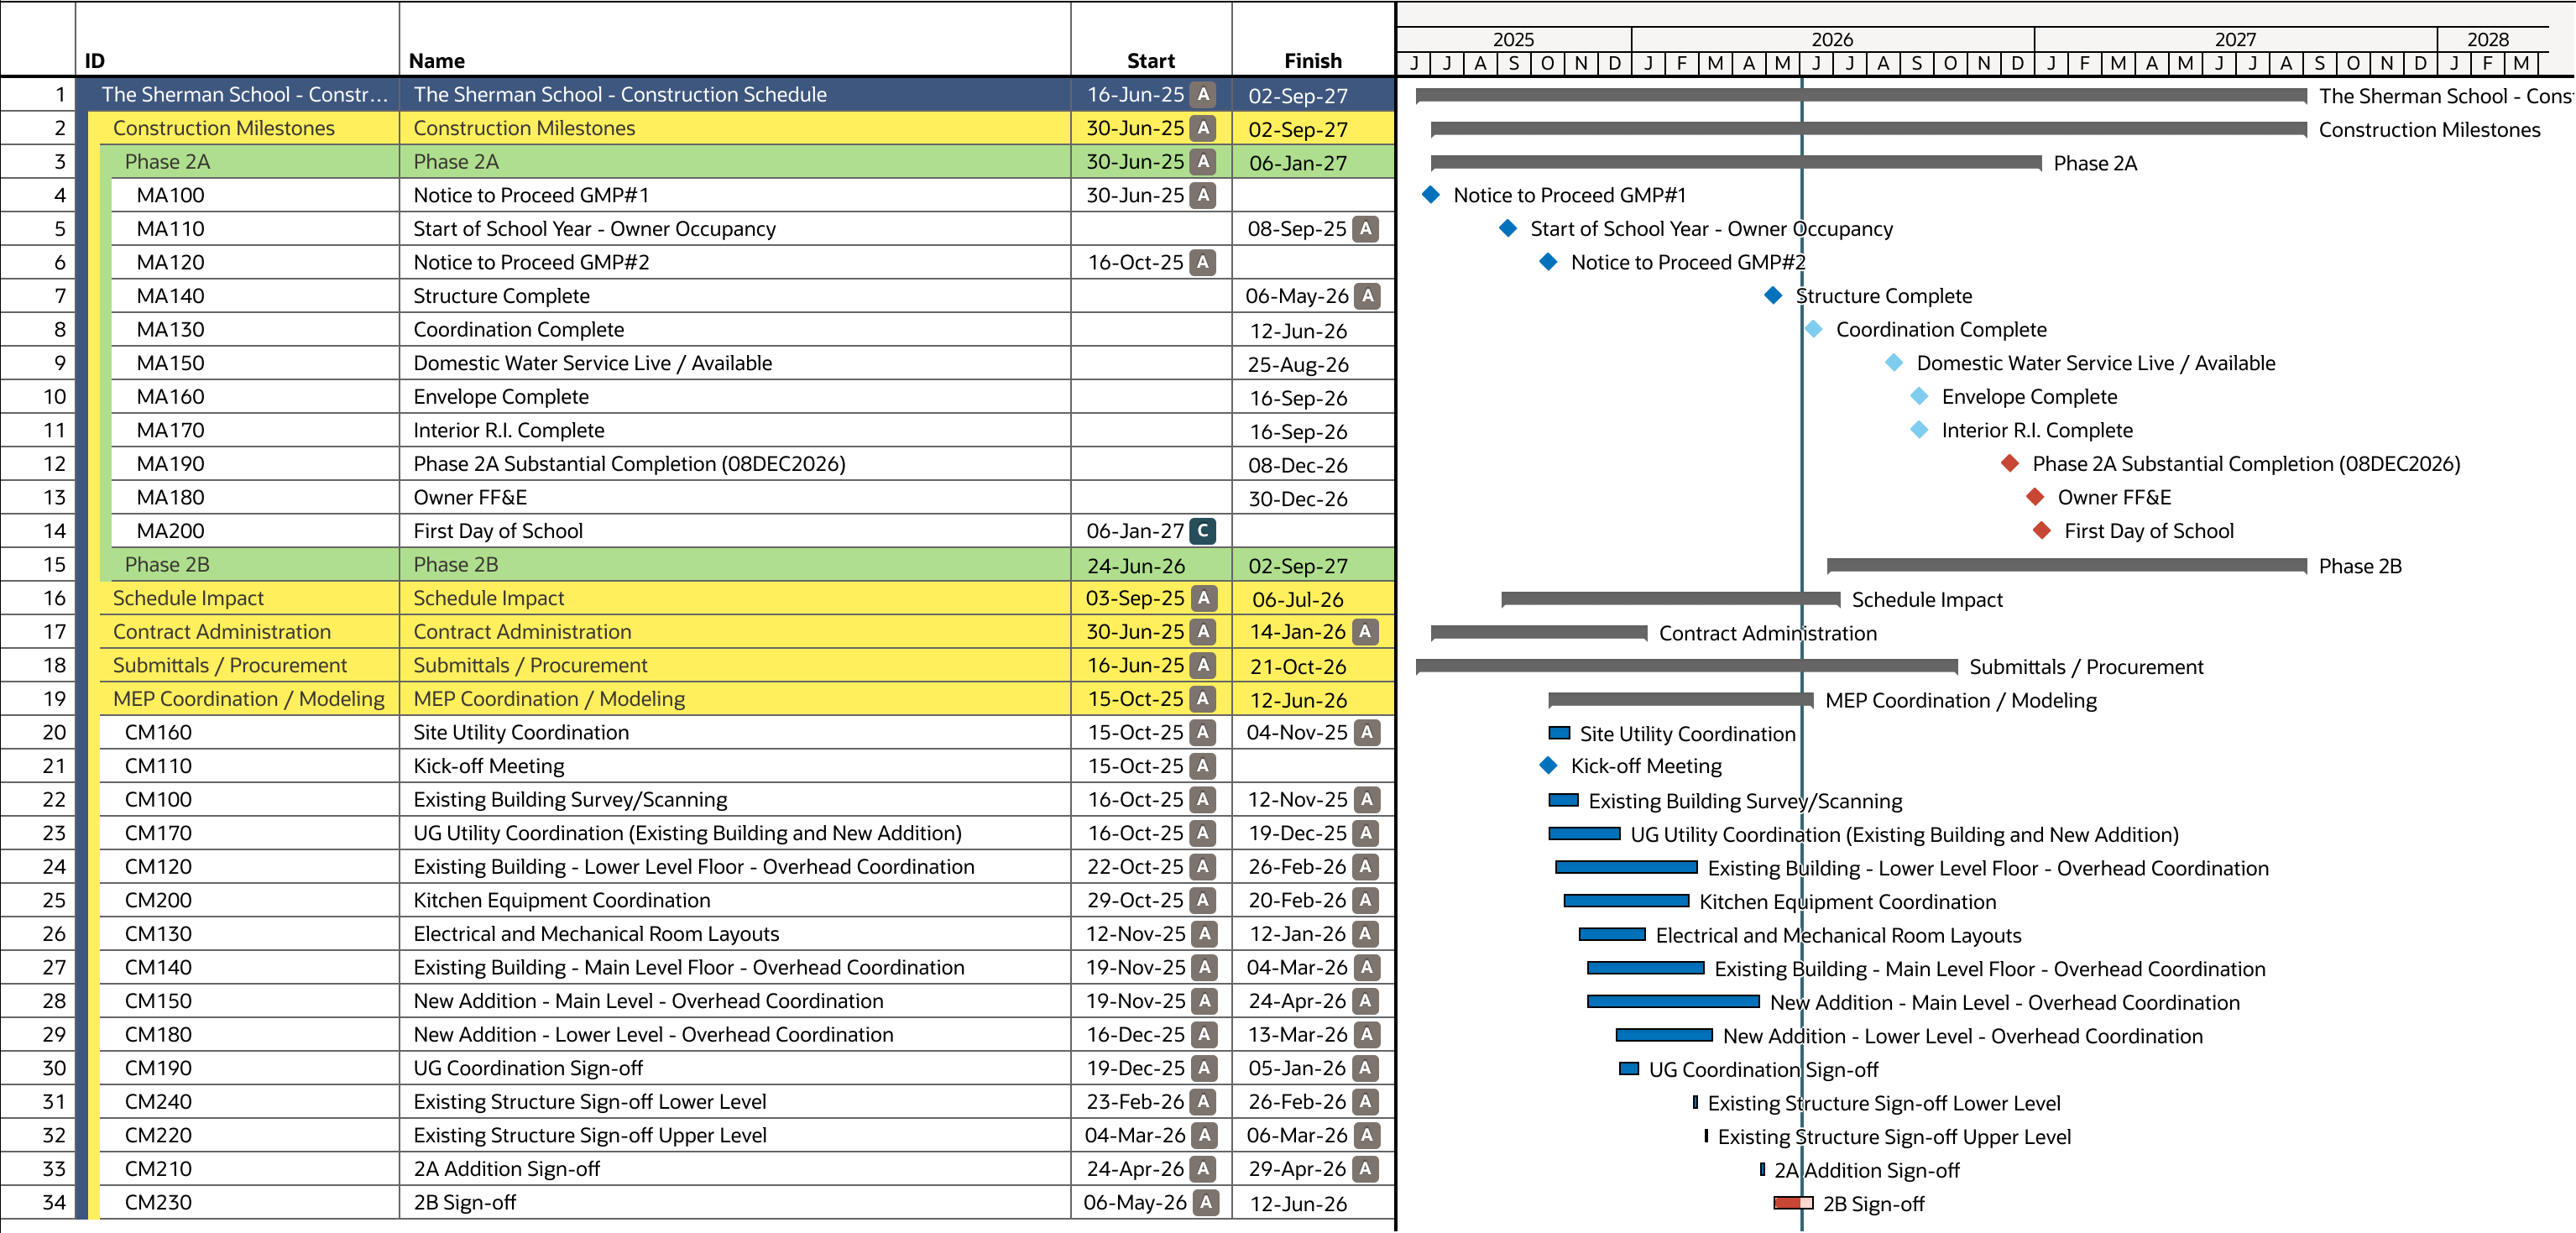

Project ID: 24-014
Prepared By: Ben Chasse
06-Jun-26 10:25 a.m.
01-Jun-26

Page: 2 of 19

Current

Progress

Critical

Milestones

Summary



The Sherman School - Construction Schedule
Data Date: 01-Jun-26




	ID	Name	Start	Finish	2025														2026														2027														2028						
					J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M															
69		S1535	Install Water Treatment Disposal System	28-May-26	A	29-May-26	A																																														
70		S1545	Backfill & Re-establish Grade Above Water Treatment Disposal System	29-May-26	A	01-Jun-26	A																																														
71		S1290	Form, Place, Finish Generator Pad	05-Jun-26		10-Jun-26																																															
72		S1300	Form, Place Finish LP Tank Pad	05-Jun-26		10-Jun-26																																															
73		S1250	Prepare Subgrade of Block Retaining Wall	05-Jun-26		10-Jun-26																																															
74		S1330	Prepare Sub grade West Playground	12-Jun-26		22-Jun-26																																															
75		S1230	PIP Foundations for Shade Canopy	22-Jun-26		30-Jun-26																																															
76		S1340	Form, Place, Finish Walkways West	22-Jun-26		02-Jul-26																																															
77		S1260	Install Block Retaining Wall / Backfill	29-Jun-26		13-Jul-26																																															
78		S1270	Prep, Form, Place, Finish Outdoor Classroom Slab	30-Jun-26		07-Jul-26																																															
79		S1380	PIP Play ground Curbing	02-Jul-26		10-Jul-26																																															
80		S1310	Form, Place, Finish Walkways North	07-Jul-26		21-Jul-26																																															
81		X8110	Layout, Cut, Grade, Stair (Alt #4)	13-Jul-26		21-Jul-26																																															
82		S1265	Reset Septic Tank Covers	13-Jul-26		15-Jul-26																																															
83		S1220	Prepare Subgrade East Elevation	15-Jul-26		23-Jul-26																																															
84		S1350	Curbing Parent Loop North-West	21-Jul-26		29-Jul-26																																															
85		X9910	Form, Place, Finish Stair (Alt #4)	21-Jul-26		25-Aug-26																																															
86		S1280	Prep, Form, Place East Retaining Wall Foundation	23-Jul-26		31-Jul-26																																															
87		X8060	Prepare Subgrade for Emergency Access Area	23-Jul-26		30-Jul-26																																															
88		S1370	Planter Foundations	29-Jul-26		05-Aug-26																																															
89		X8070	Prepare Subgrade East Elevation Playscape	29-Jul-26		07-Aug-26																																															
90		X8240	Form, Place, Finish Emergency Access Walkway	30-Jul-26		11-Aug-26																																															
91		S1390	Island Curbing Parent Loop	05-Aug-26		12-Aug-26																																															
92		X8100	Install Basket Ball Hoops / Foundations	07-Aug-26		17-Aug-26																																															
93		X8190	Curbing at Playground East	07-Aug-26		18-Aug-26																																															
94		X8270	Form / Pour Entrance Stair S.E.	11-Aug-26		21-Aug-26																																															
95		S1410	Install Curbing East Lot	12-Aug-26		21-Aug-26																																															
96		X8220	Fine Grade, Prep, Pave, Hardscape Court	18-Aug-26		25-Aug-26																																															
97		X8330	Rubber Surfacing at Playscape East	18-Aug-26		28-Aug-26																																															
98		S1360	Prepare Sub Grade Walkway East Lot	21-Aug-26		28-Aug-26																																															
99		S1320	Form, Place, Finish Walkways East	21-Aug-26		02-Sep-26																																															
100		X8360	SS. Hand Rails @ Stairway (Alt#4)	25-Aug-26		03-Sep-26																																															
101		S1450	Stamped Concrete Parent Loop	01-Sep-26		10-Sep-26																																															
102		S1420	Rough Grade Parent Loop & Hardscape	02-Sep-26		10-Sep-26																																															



The Sherman School - Construction Schedule
Data Date: 01-Jun-26



	ID	Name	Start	Finish	2025												2026												2027												2028		
					J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M					
103		X8140	Install Deep Drainage South East	02-Sep-26	24-Sep-26																									Install Deep Drainage South East													
104		X8350	Basket Ball Court Surfacing	03-Sep-26	16-Sep-26																									Basket Ball Court Surfacing													
105		X8080	Layout, Cut, Grade, Switch Back Ramp	03-Sep-26	16-Sep-26																									Layout, Cut, Grade, Switch Back Ramp													
106		S1440	Fine Grade Parent Loop & Hardscape	10-Sep-26	16-Sep-26																									Fine Grade Parent Loop & Hardscape													
107		S1470	Binder Paving Parent Loop	16-Sep-26	22-Sep-26																									Binder Paving Parent Loop													
108		S1480	Top Coat Paving Hardscape Play Area	16-Sep-26	21-Sep-26																									Top Coat Paving Hardscape Play Area													
109		X8210	Form, Place, Finish Swictback Ramp	16-Sep-26	02-Oct-26																									Form, Place, Finish Swictback Ramp													
110		S1400	Form, Place, Finish Walkway East Lot	24-Sep-26	06-Oct-26																									Form, Place, Finish Walkway East Lot													
111		X8340	Site Rails @ Ramp	02-Oct-26	13-Oct-26																									Site Rails @ Ramp													
112		S1430	Reclaim Existing Asphalt	06-Oct-26	09-Oct-26																									Reclaim Existing Asphalt													
113		S1460	Rough Grade Subbase East Lot	09-Oct-26	16-Oct-26																									Rough Grade Subbase East Lot													
114		S1490	Fine Grade for Paving East Lot	16-Oct-26	23-Oct-26																									Fine Grade for Paving East Lot													
115		S1500	Binder Pave East Lot	23-Oct-26	28-Oct-26																									Binder Pave East Lot													
116		S1510	Top Coat Paving East Lot	28-Oct-26	04-Nov-26																									Top Coat Paving East Lot													
117		Landscape & Furnishings	Landscape & Furnishings	21-Jul-26	24-Nov-26																									Landscape & Furnishings													
118		S1520	Deliver, Install Canopy Structure	21-Jul-26	28-Jul-26																									Deliver, Install Canopy Structure													
119		S1550	Guard Rails & Fence @ Parent Loop	25-Aug-26	01-Sep-26																									Guard Rails & Fence @ Parent Loop													
120		S1530	Install Wood Guard Rail East Lot	28-Aug-26	09-Sep-26																									Install Wood Guard Rail East Lot													
121		S1570	Install Light Poles and Bollards	10-Sep-26	22-Sep-26																									Install Light Poles and Bollards													
122		S1540	Install Play Equipment West	17-Sep-26	01-Oct-26																									Install Play Equipment West													
123	S1590	Playground State Compliance Testing	22-Sep-26	29-Sep-26																									Playground State Compliance Testing														
124	S1560	Rubber Surfacing W. Play Ground	01-Oct-26	12-Oct-26																									Rubber Surfacing W. Play Ground														
125	S1580	Install Playground Fencing & Gates West	12-Oct-26	21-Oct-26																									Install Playground Fencing & Gates West														
126	S1600	Site Signage	28-Oct-26	04-Nov-26																									Site Signage														
127	S1610	Landscaping	28-Oct-26	09-Nov-26																									Landscaping														
128	S1620	Pavement Markings	04-Nov-26	10-Nov-26																									Pavement Markings														
129	S1630	Site Completion List	10-Nov-26	24-Nov-26																									Site Completion List														
130	Demolition of Existing Str...	Demolition of Existing Structures	01-Aug-25	24-Dec-25																									Demolition of Existing Structures														
131	Structure	Structure	11-Dec-25	21-Aug-26																									Structure														
132	Addition Foundation	Addition Foundation	11-Dec-25	13-Mar-26																									Addition Foundation														
133	Lower Level Existing Str...	Lower Level Existing Structure	29-Dec-25	21-Aug-26																									Lower Level Existing Structure														
134	X1230	Install Reinforcing Angles to Support Structure AW-AS x A6-A13	29-Dec-25	21-Jan-26																									Install Reinforcing Angles to Support Structure AW-AS x A6-A13														
135	X1240	Exc.& Prepare Subgrade N. Entrance NP.3 - AS x N22-A3	05-Jan-26	07-Jan-26																									Exc.& Prepare Subgrade N. Entrance NP.3 - AS x N22-A3														
136	X1250	Remove Existing Footings AW-AS x A6-A13	21-Jan-26	03-Feb-26																									Remove Existing Footings AW-AS x A6-A13														

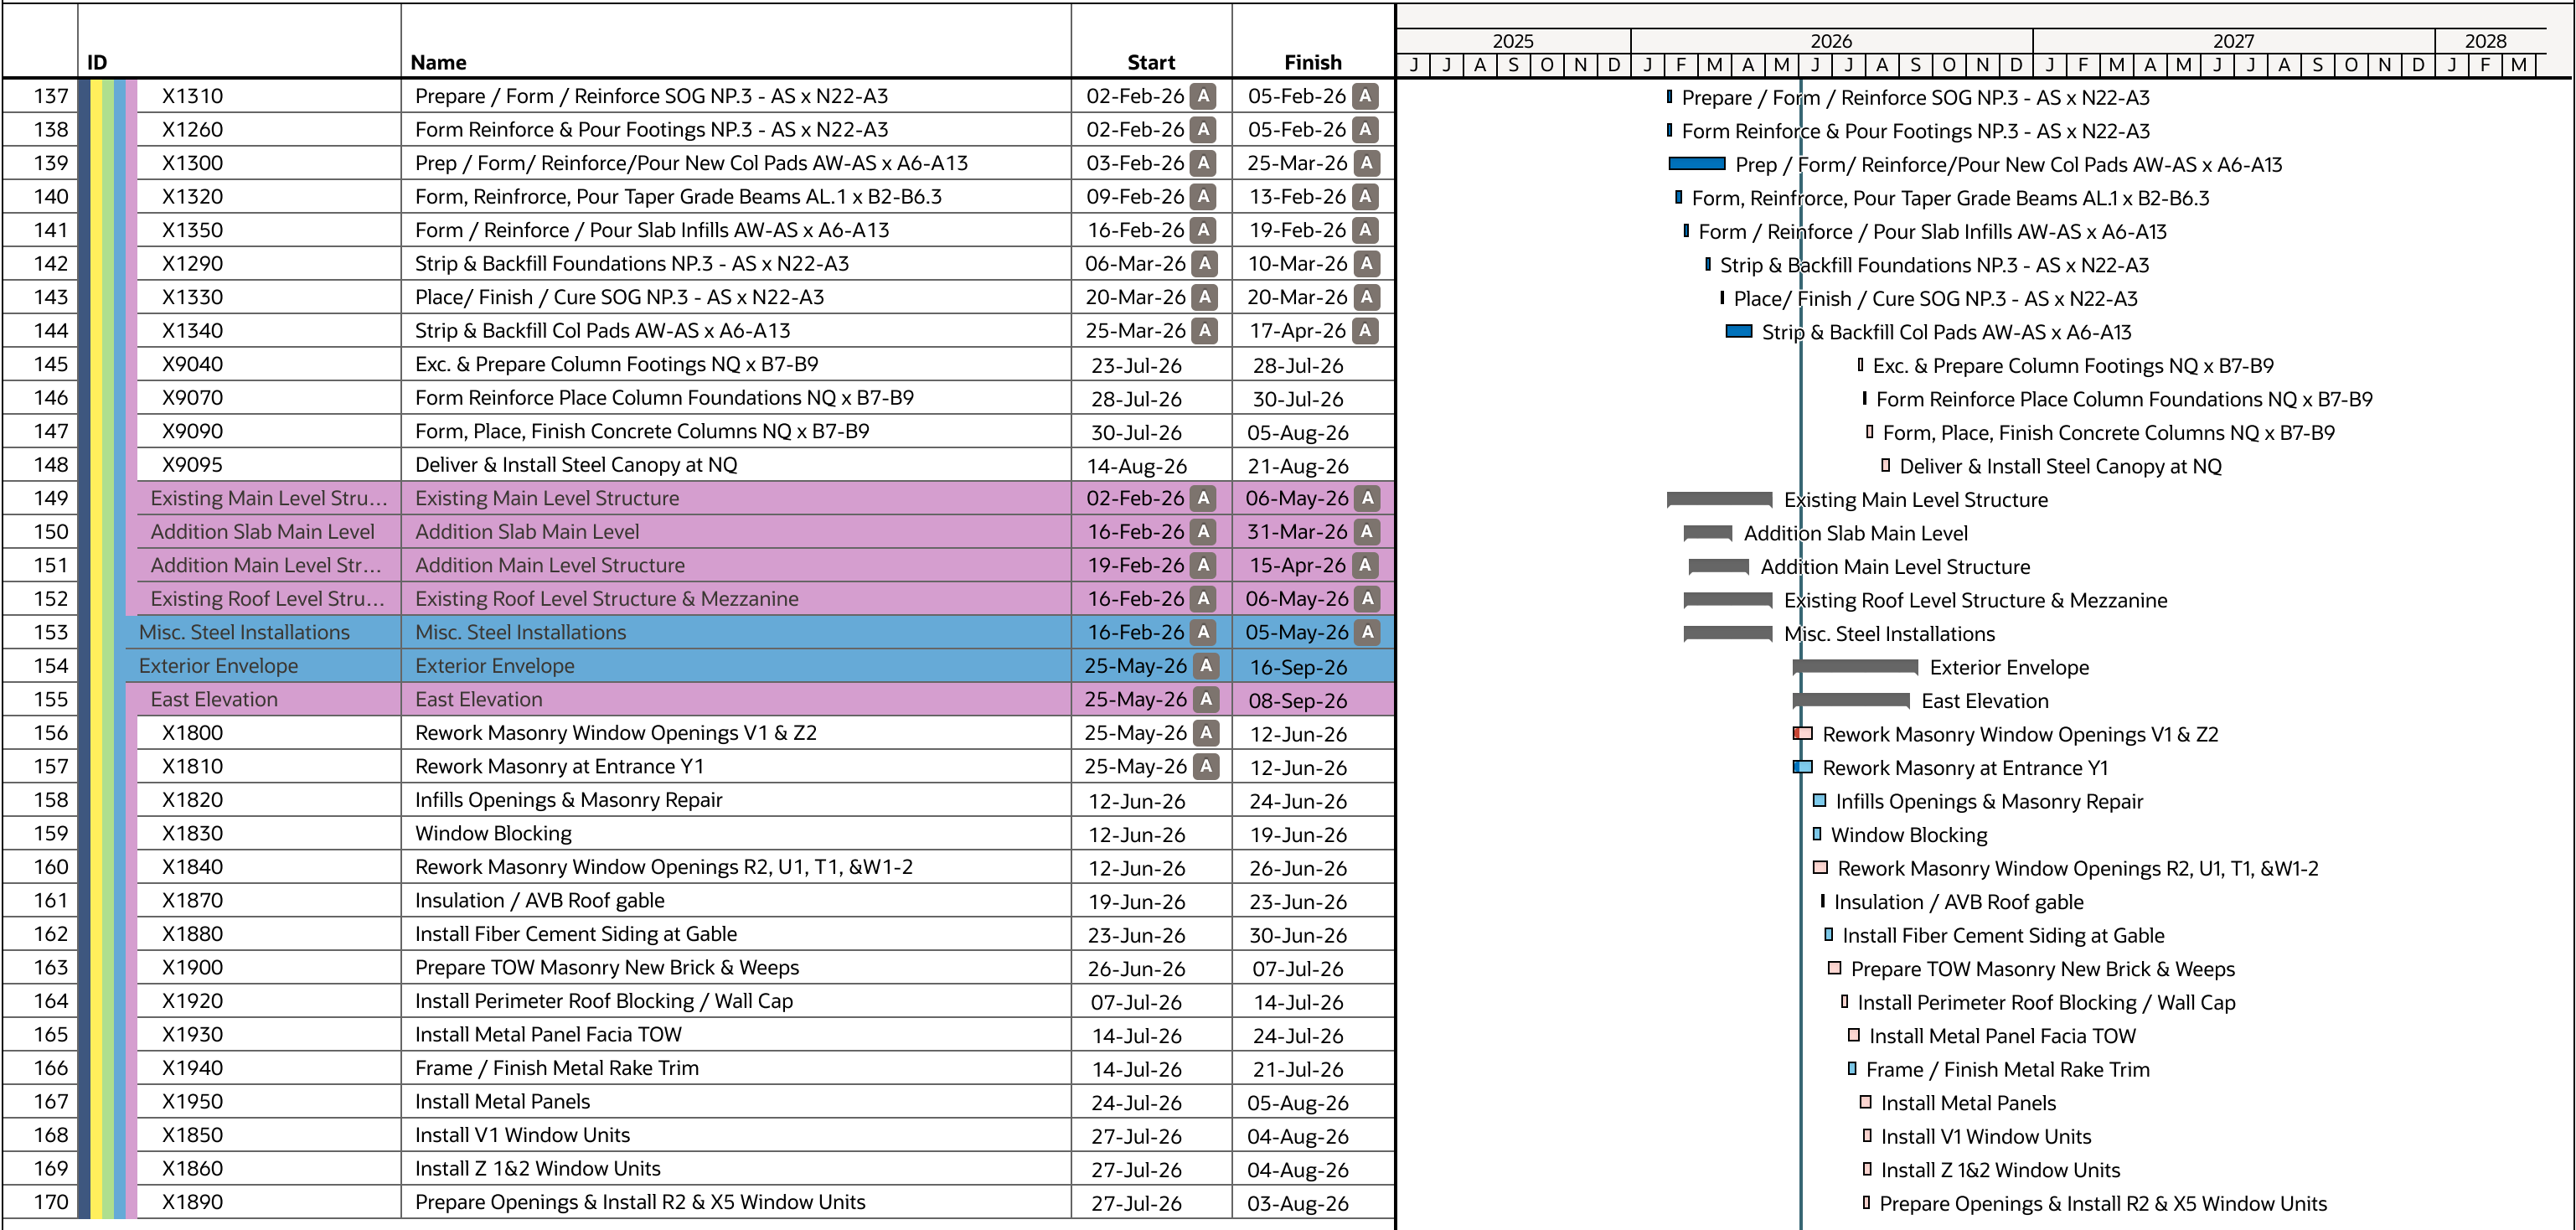



The Sherman School - Construction Schedule
Data Date: 01-Jun-26




	ID	Name	Start	Finish	2025														2026														2027														2028			
					J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M												
171		X1960	Frame / Finish Metal Facia Trim	05-Aug-26	12-Aug-26																													▣ Frame / Finish Metal Facia Trim																
172		X1910	Install Solarium Glazing W2	01-Sep-26	08-Sep-26																													▣ Install Solarium Glazing W2																
173		North Elevation Admin ...	North Elevation Admin / Media Center	29-May-26	A	26-Aug-26																													▣ North Elevation Admin / Media Center															
174		X1970	CFMF / Sheathing Vestibule A3- N22 x NP.3- NR.9	29-May-26	A	12-Jun-26																													▣ CFMF / Sheathing Vestibule A3- N22 x NP.3- NR.9															
175		X1980	Insulation / AVB	12-Jun-26	19-Jun-26																													▣ Insulation / AVB																
176		X1990	Brick Masonry A3- N22 x AJ - AS	19-Jun-26	26-Jun-26																													▣ Brick Masonry A3- N22 x AJ - AS																
177		X2010	Pointing / Patching Existing Brick	26-Jun-26	06-Jul-26																													▣ Pointing / Patching Existing Brick																
178		X2000	Install A2, B, C1, C2 Window Units	04-Aug-26	11-Aug-26																													▣ Install A2, B, C1, C2 Window Units																
179		X2020	Install Entrance Door A1	11-Aug-26	14-Aug-26																													▣ Install Entrance Door A1																
180		X2030	Frame / Finish Metal Rake Trim	12-Aug-26	19-Aug-26																													▣ Frame / Finish Metal Rake Trim																
181		X2040	Install FC Siding	19-Aug-26	26-Aug-26																													▣ Install FC Siding																
182		West Elevation Admin / ...	West Elevation Admin / Media Center	25-May-26	A	21-Jul-26																													▣ West Elevation Admin / Media Center															
183		X2050	CFMF / Sheathing Vestibule AG x A16-A3.5	25-May-26	A	12-Jun-26																													▣ CFMF / Sheathing Vestibule AG x A16-A3.5															
184		X2060	Insulation / AVB	12-Jun-26	18-Jun-26																													▣ Insulation / AVB																
185		X2070	Install D1, D2, D3, E2, F1, F2, F3 Window Units	18-Jun-26	25-Jun-26																													▣ Install D1, D2, D3, E2, F1, F2, F3 Window Units																
186		X2090	Frame / Finish Metal Rake Trim	25-Jun-26	06-Jul-26																													▣ Frame / Finish Metal Rake Trim																
187		X2080	Install Storefront door	25-Jun-26	30-Jun-26																													▣ Install Storefront door																
188		X2100	Pointing / Patching Existing Brick	06-Jul-26	14-Jul-26																													▣ Pointing / Patching Existing Brick																
189		X2110	Install FC Siding	14-Jul-26	21-Jul-26																													▣ Install FC Siding																
190		West Elevation / First Gr...	West Elevation / First Grade Addition	25-May-26	A	04-Sep-26																													▣ West Elevation / First Grade Addition															
191		X2120	CFMF / Sheathing N8-N1 x NA-NE	25-May-26	A	12-Jun-26																													▣ CFMF / Sheathing N8-N1 x NA-NE															
192		X2140	Insulation / AVB	12-Jun-26	22-Jun-26																													▣ Insulation / AVB																
193		X2130	CFMF at N4-C4 Gym	12-Jun-26	19-Jun-26																													▣ CFMF at N4-C4 Gym																
194		X2150	Install X4 Window Units Gym	19-Jun-26	26-Jun-26																													▣ Install X4 Window Units Gym																
195		X2160	Install P Window Units	22-Jun-26	29-Jun-26																													▣ Install P Window Units																
196		X2170	Install J Window Units	29-Jun-26	02-Jul-26																													▣ Install J Window Units																
197		X2180	Frame / Finish Metal Rake Trim	29-Jun-26	08-Jul-26																													▣ Frame / Finish Metal Rake Trim																
198		X2190	Brick Masonry	02-Jul-26	17-Jul-26																													▣ Brick Masonry																
199		X2200	Insulated Metal Panels / Soffits	17-Jul-26	31-Jul-26																													▣ Insulated Metal Panels / Soffits																
200		X2220	Install Entrance Door N1	31-Jul-26	05-Aug-26																													▣ Install Entrance Door N1																
201		X2210	Install FC Siding	26-Aug-26	04-Sep-26																													▣ Install FC Siding																
202		South Elevation First Gr...	South Elevation First Grade Addition	25-May-26	A	16-Sep-26																													▣ South Elevation First Grade Addition															
203		X2230	CFMF / Sheathing N1 x NN-NA	25-May-26	A	12-Jun-26																													▣ CFMF / Sheathing N1 x NN-NA															
204		X2240	Insulation / AVB	12-Jun-26	19-Jun-26																													▣ Insulation / AVB																



The Sherman School - Construction Schedule
Data Date: 01-Jun-26



	ID		Name	Start	Finish																												
						2025							2026							2027							2028						
						J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S
205		X2250	Brick Masonry	19-Jun-26	08-Jul-26															Brick Masonry													
206		X2260	Install L, M Window Units	08-Jul-26	15-Jul-26															Install L, M Window Units													
207		X2270	Insulated Metal Panels / Soffits	08-Jul-26	22-Jul-26															Insulated Metal Panels / Soffits													
208		X2280	Frame / Finish Metal Trim	15-Jul-26	23-Jul-26															Frame / Finish Metal Trim													
209		X2290	Install FC Siding	04-Sep-26	16-Sep-26															Install FC Siding													
210		North Elevation Courtyard	North Elevation Courtyard	12-Jun-26	14-Jul-26															North Elevation Courtyard													
211		X2300	CMU A16.1 x AB-AE	12-Jun-26	18-Jun-26															CMU A16.1 x AB-AE													
212		X2310	Insulation / AVB	18-Jun-26	23-Jun-26															Insulation / AVB													
213		X2320	Brick Masonry	23-Jun-26	29-Jun-26															Brick Masonry													
214		X2330	Install G & H Window Units	29-Jun-26	02-Jul-26															Install G & H Window Units													
215		X2340	Frame / Finish Metal Panel & Facia	29-Jun-26	14-Jul-26															Frame / Finish Metal Panel & Facia													
216		East Elevation First Grad...	East Elevation First Grade Addition	12-Jun-26	16-Sep-26															East Elevation First Grade Addition													
217		X2350	CFMF / Sheathing AB x N1-N3	12-Jun-26	19-Jun-26															CFMF / Sheathing AB x N1-N3													
218		X2360	Insulation / AVB	19-Jun-26	25-Jun-26															Insulation / AVB													
219		X2370	Brick Masonry	25-Jun-26	02-Jul-26															Brick Masonry													
220		X2390	Frame / Finish Metal Rake Trim	02-Jul-26	17-Jul-26															Frame / Finish Metal Rake Trim													
221		X2380	Install J, K Window Units	07-Jul-26	13-Jul-26															Install J, K Window Units													
222		X2400	Install FC Siding	21-Jul-26	30-Jul-26															Install FC Siding													
223		X2410	Envelope Complete		16-Sep-26															Envelope Complete													
224		Roofing 2A	Roofing 2A	28-Apr-26 A	08-Oct-26															Roofing 2A													
225		Existing Slope Roof North	Existing Slope Roof North	12-Jun-26	21-Sep-26															Existing Slope Roof North													
226		X3000	Strip shingles to deck	12-Jun-26	22-Jun-26															Strip shingles to deck													
227		X3010	Select Demolition Rake / Facia	22-Jun-26	02-Jul-26															Select Demolition Rake / Facia													
228		X3020	Inspect Repair Roof Deck / Dry-in	22-Jun-26	26-Jun-26															Inspect Repair Roof Deck / Dry-in													
229		X3030	Remove / Replace Skylight	26-Jun-26	06-Jul-26															Remove / Replace Skylight													
230		X3040	Install Ridge Venting	26-Jun-26	02-Jul-26															Install Ridge Venting													
231		X3050	Install Steel Plates & Angle Support	02-Jul-26	29-Jul-26															Install Steel Plates & Angle Support													
232		X3060	Install Edge Blocking & Vert Insulation	29-Jul-26	19-Aug-26															Install Edge Blocking & Vert Insulation													
233		X3070	Metal Trim Rake / Facia	19-Aug-26	28-Aug-26															Metal Trim Rake / Facia													
234		X3080	Install GFR Shingles	28-Aug-26	09-Sep-26															Install GFR Shingles													
235		X3090	Install Gutter / Leader Drains	09-Sep-26	21-Sep-26															Install Gutter / Leader Drains													
236		Gym Roof (A- 1R1.B)	Gym Roof (A- 1R1.B)	13-Jul-26	08-Sep-26															Gym Roof (A-1R1.B)													
237		X3100	Select Demolition Perimeter / Dry-in	13-Jul-26	22-Jul-26															Select Demolition Perimeter / Dry-in													
238		X3110	Remove Existing Curbs and Fixtures / Dry-in	22-Jul-26	29-Jul-26															Remove Existing Curbs and Fixtures / Dry-in													

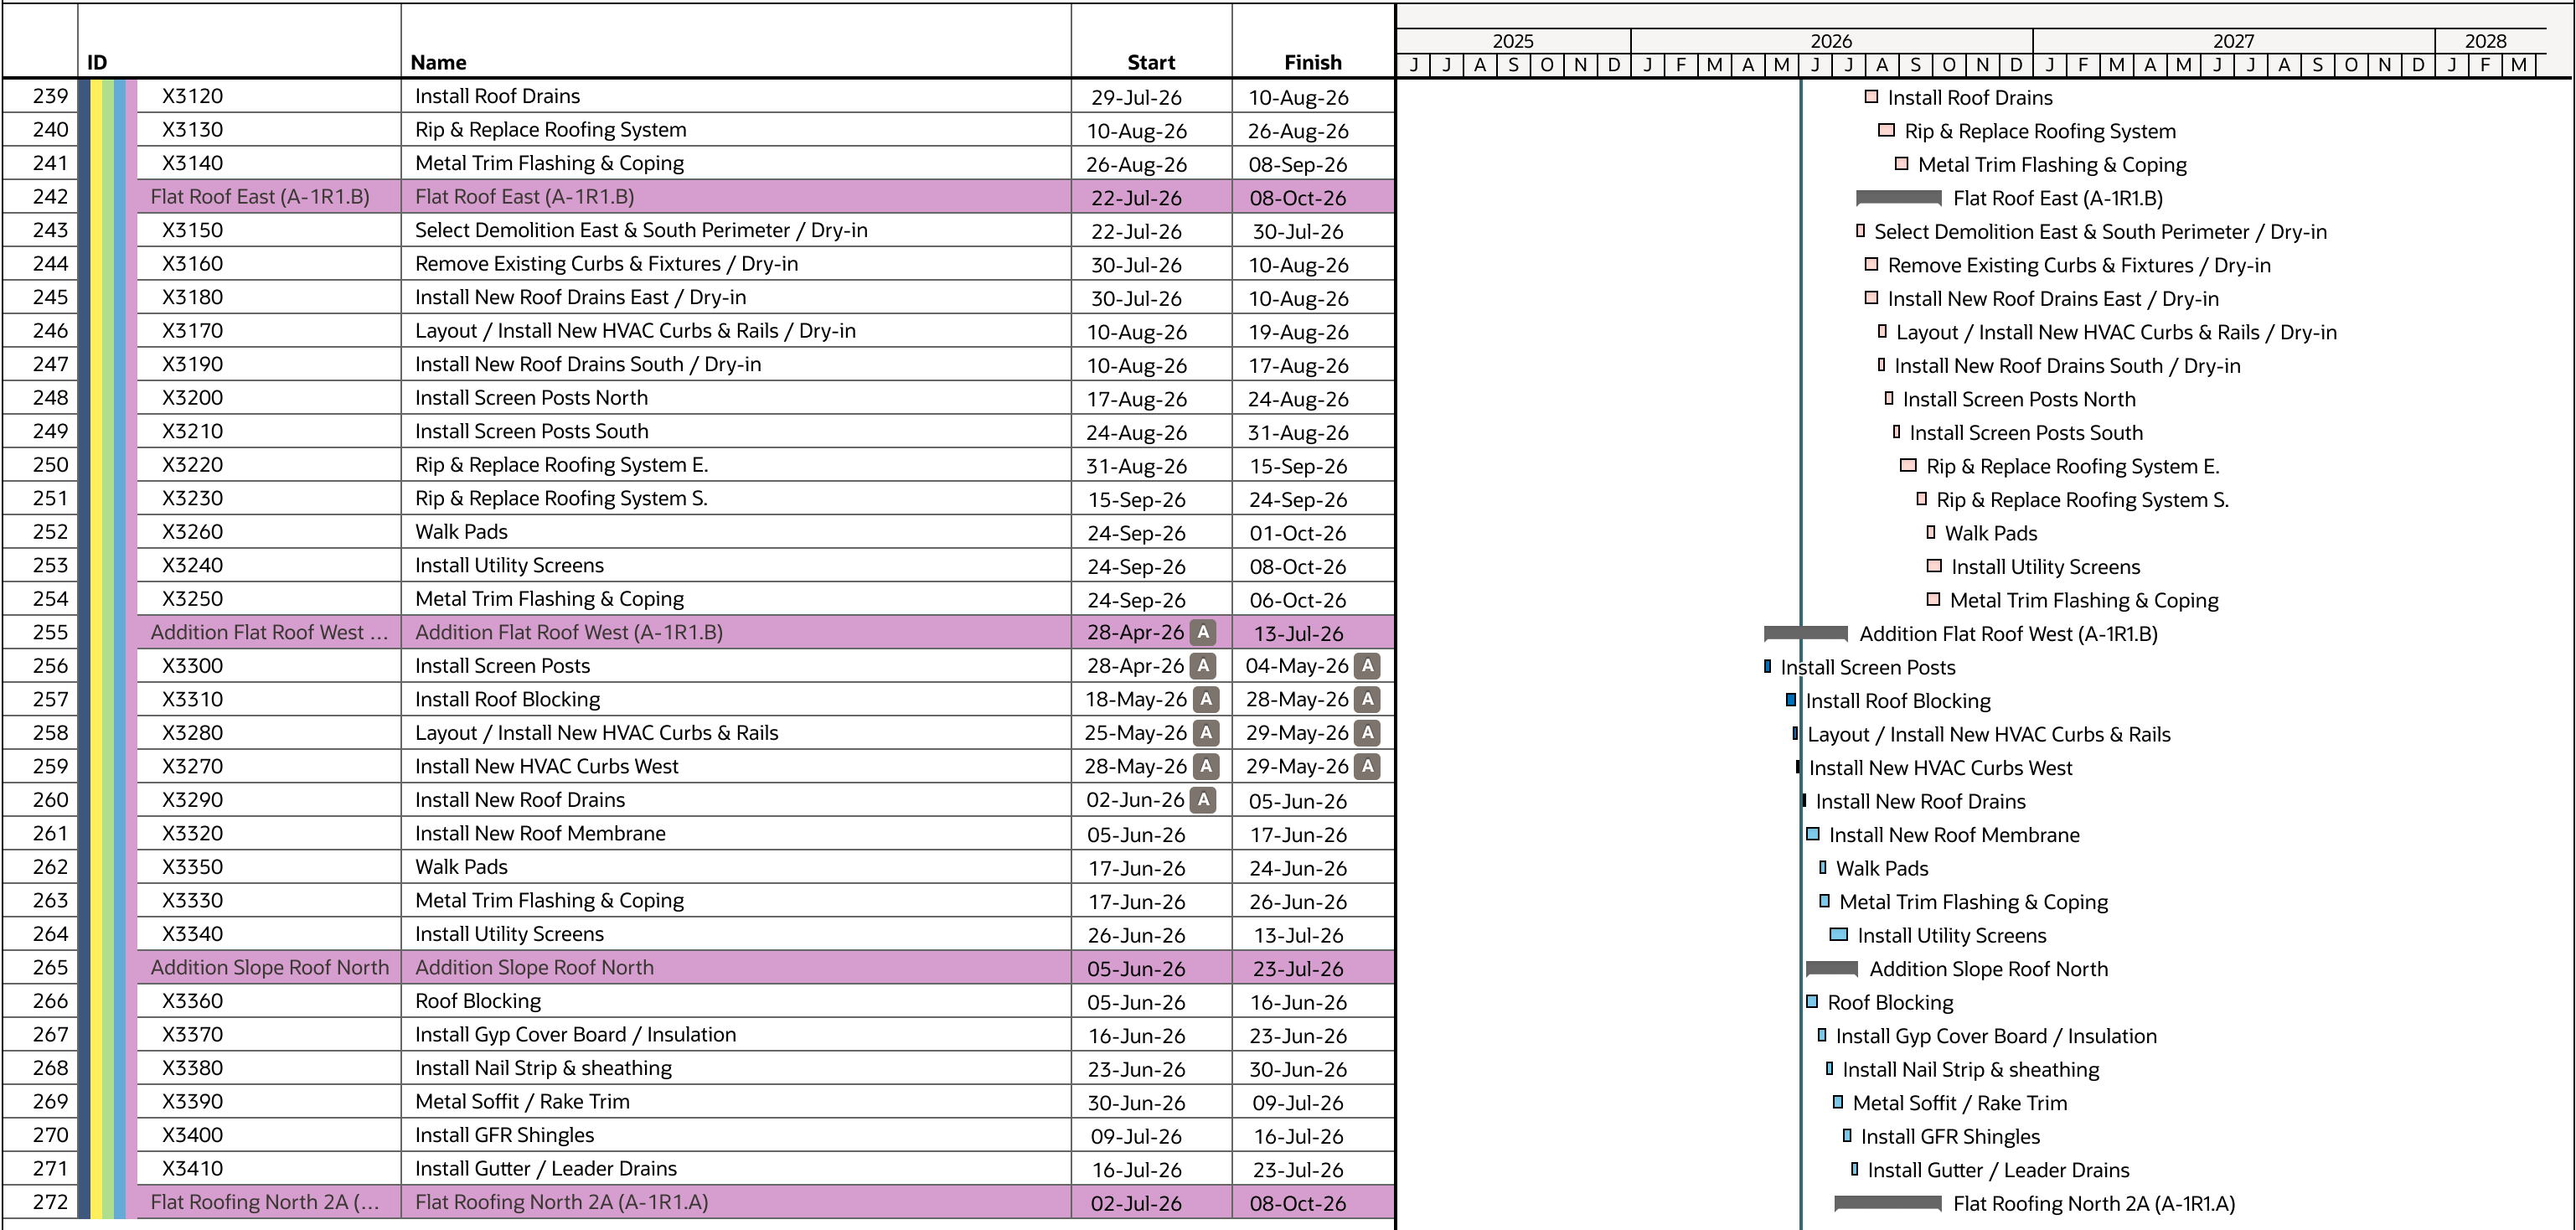



□ Select Demolition East Perimeter / Dry-in
 □ Remove Existing Curbs and Fixtures / Dry-in
 □ Install New Roof Drains East / Dry-in
 □ Layout / Install New HVAC Curbs East / Dry-in
 □ Install Screen Posts North
 □ Install New Roof Drains South / Dry-in
 □ Layout / Install New HVAC Curbs & Rails South / Dry-in
 □ Install Screen Posts South
 □ Rip & Replace Roofing System N.E.
 □ Rip & Replace Roofing System S.E.
 □ Rip & Replace Roofing System S.
 □ Install Utility Screens
 □ Metal Trim Flashing & Coping
 □ Walk Pads
 ◆ 2A Roofing Complete
 Interior Rough
 MEP R.I.
 Lower Level North 2A (A-100.A)
 UG Slab Plumbing / Elec. RI AJ-AW x A1-A12
 CMU Wall R.I. AJ-AW x A12-A17
 UG Slab Plumbing / Elec. RI AJ-AW x A12-A17
 CMU Wall R.I. AJ-AW x A1-A12
 MEP OH R.I. AJ-AW x A1-A12
 Fire Protection R.I. AJ-AW x A1-A12
 CFMF Wall R.I. AJ-AW x A12-A17
 CFMF Wall R.I. AJ-AW x A1-A12
 MEP OH R.I. AJ-AW x A12-A17
 Fire Protection R.I. AJ-AW x A12-A17
 Elevator
 Install New Control Equipment
 R.I. Hoistway
 Refurbish Car
 Main Level North 2A (A-101.A)
 MEP OH R.I. AB-AW x A1-A17

Project ID: 24-014
Prepared By: Ben Chasse
06-Jun-26 10:25 a.m.
01-Jun-26

 Current
  Milestones
 Progress
  Summary
 Critical



The Sherman School - Construction Schedule
Data Date: 01-Jun-26



	ID	Name	Start	Finish																															
					2025							2026							2027							2028									
					J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D
307		X4125	Fire Protection R.I. AB-AW x A1-A17	20-Apr-26	A	01-May-26	A	Fire Protection R.I. AB-AW x A1-A17																											
308		X4140	CFMF Wall R.I. AB-AW x A1-A17	23-Apr-26	A	08-May-26	A	CFMF Wall R.I. AB-AW x A1-A17																											
309		X4130	CMU Wall R.I AB-AW x A1-A17	23-Apr-26	A	06-May-26	A	CMU Wall R.I AB-AW x A1-A17																											
310		Main Level South 2A (...)	Main Level South 2A (A-101.B)	23-Feb-26	A	27-Jul-26	Main Level South 2A (A-101.B)																												
311		X4150	MEP OH R.I. AB-AW x A17-B7	23-Feb-26	A	15-Jun-26	MEP OH R.I. AB-AW x A17-B7																												
312		X4170	CFMF Wall R.I. AB-AW x A17-B7	28-Apr-26	A	15-Jun-26	CFMF Wall R.I. AB-AW x A17-B7																												
313		X4160	CMU Wall R.I AB-AW x A17-B7	19-Jun-26		06-Jul-26	CMU Wall R.I AB-AW x A17-B7																												
314		X4155	Fire Protection R.I. AB-AW x A17-B7	06-Jul-26		27-Jul-26	Fire Protection R.I. AB-AW x A17-B7																												
315		Lower Level South 2A (...)	Lower Level South 2A (A-100.B)	05-Jan-26	A	25-Aug-26	Lower Level South 2A (A-100.B)																												
316		X4180	UG Slab Plumbing / Elec. R.I. NE-BP x A17-B7	05-Jan-26	A	20-Feb-26	A	UG Slab Plumbing / Elec. R.I. NE-BP x A17-B7																											
317	X4190	UG Slab R.I. Cafe / Kitchen	12-Jan-26	A	20-Feb-26	A	UG Slab R.I. Cafe / Kitchen																												
318	X4200	MEP OH R.I. NE-BP x A17-B7	20-Feb-26	A	19-Jun-26	MEP OH R.I. NE-BP x A17-B7																													
319	X4210	Receive / Install Electric Gear	13-Apr-26	A	21-May-26	A	Receive / Install Electric Gear																												
320	X4220	CMU Wall R.I. NE-BP x A17-B7	28-Apr-26	A	19-Jun-26	CMU Wall R.I. NE-BP x A17-B7																													
321	X4250	Receive / Install ATS	22-May-26	A	25-Jun-26	Receive / Install ATS																													
322	X4230	CFMF Wall R.I. NE-BP x A17-B7	19-Jun-26		06-Jul-26	CFMF Wall R.I. NE-BP x A17-B7																													
323	X4270	Receive / Install Motor Generator	26-Jun-26		02-Jul-26	Receive / Install Motor Generator																													
324	X4215	Fire Protection R.I. NE-BP x A17-B7	26-Jun-26		13-Jul-26	Fire Protection R.I. NE-BP x A17-B7																													
325	X4260	MEP R.I. Water Room / Maint. 1058 - 1059	10-Jul-26		14-Aug-26	MEP R.I. Water Room / Maint. 1058 - 1059																													
326	X4240	Permanent Tie-in to Existing MDF	13-Jul-26		17-Jul-26	Permanent Tie-in to Existing MDF																													
327	X4275	Fire Protection R.I. Water Room / Maint. 1058 - 1059	07-Aug-26		14-Aug-26	Fire Protection R.I. Water Room / Maint. 1058 - 1059																													
328	X4280	Potability Testing	14-Aug-26		25-Aug-26	Potability Testing																													
329	X4290	Domestic Water Service Live / Available			25-Aug-26	Domestic Water Service Live / Available																													
330	Main Level Addition So...	Main Level Addition South 2A (A-101.A)	16-Apr-26	A	10-Jul-26	Main Level Addition South 2A (A-101.A)																													
331	X4300	MEP OH R.I. AB-AW x A17-B7	16-Apr-26	A	01-Jul-26	MEP OH R.I. AB-AW x A17-B7																													
332	X4310	CMU Wall R.I AB-AW x A17-B7	11-May-26	A	29-May-26	A	CMU Wall R.I AB-AW x A17-B7																												
333	X4320	CFMF Wall R.I. AB-AW x A17-B7	26-May-26	A	10-Jul-26	CFMF Wall R.I. AB-AW x A17-B7																													
334	X4305	Fire Protection OH R.I. AB-AW x A17-B7	29-Jun-26		08-Jul-26	Fire Protection OH R.I. AB-AW x A17-B7																													
335	Lower Level North 2A R...	Lower Level North 2A Rough (A-100.A)	05-Jan-26	A	21-Jul-26	Lower Level North 2A Rough (A-100.A)																													
336	X4420	CMU Masonry AJ-AW x A12 x A17	05-Jan-26	A	30-Jan-26	A	CMU Masonry AJ-AW x A12 x A17																												
337	X4330	Back fill, Prep, Reinforce Slab Infills AJ-AW x A1-A12	12-Jan-26	A	06-Feb-26	A	Back fill, Prep, Reinforce Slab Infills AJ-AW x A1-A12																												
338	X4340	Back fill, Prep, Reinforce Slab Infills AJ-AW x A12-A17	12-Jan-26	A	21-Jan-26	A	Back fill, Prep, Reinforce Slab Infills AJ-AW x A12-A17																												
339	X4350	Place, Finish, Cure Slab Infills AJ-AW x A12-A17	16-Jan-26	A	22-Jan-26	A	Place, Finish, Cure Slab Infills AJ-AW x A12-A17																												
340	X4360	Place, Finish, Cure Slab Infills AJ-AW x A1-A12	06-Feb-26	A	12-Feb-26	A	Place, Finish, Cure Slab Infills AJ-AW x A1-A12																												



Project ID: 24-014
Prepared By: Ben Chasse
06-Jun-26 10:25 a.m.
01-Jun-26

Page: 11 of 19

Current

Progress

Critical

Milestones

Summary



The Sherman School - Construction Schedule
Data Date: 01-Jun-26



	ID	Name	Start	Finish																															
					2025							2026							2027							2028									
					J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D
375		X4680	Install Door Frames AB-AW x A1-A17	13-Apr-26	A	16-Apr-26	A	I Install Door Frames AB-AW x A1-A17																											
376		X4700	CFMF AB-AW x A1-A17	16-Apr-26	A	29-Apr-26	A	■ CFMF AB-AW x A1-A17																											
377		X4690	CMU Masonry AB-AW x A1-A17	17-Apr-26	A	28-Apr-26	A	■ CMU Masonry AB-AW x A1-A17																											
378		X4720	Drywall /Finish AB-AW x A1-A17	28-Apr-26	A	15-May-26	A	■ Drywall /Finish AB-AW x A1-A17																											
379		X4710	Blocking / Backing AB-AW x A1-A17	30-Apr-26	A	06-May-26	A	■ Blocking / Backing AB-AW x A1-A17																											
380		X4730	CFMF Hard Ceilings / Soffits AB-AW x A1-A17	06-Jul-26		16-Jul-26		■ CFMF Hard Ceilings / Soffits AB-AW x A1-A17																											
381		Main Level Addition Nor...	Main Level Addition North 2A Rough (A101.A)	13-Apr-26	A	28-Jul-26		■ Main Level Addition North 2A Rough (A101.A)																											
382		X4750	CMU Masonry NC-NN x N4-N8	13-Apr-26	A	13-May-26	A	■ CMU Masonry NC-NN x N4-N8																											
383		X4740	Install Door Frames NC-NN x N4-N8	13-Apr-26	A	15-May-26	A	■ Install Door Frames NC-NN x N4-N8																											
384		X4760	CFMF NC-NN x N4-N8	12-Jun-26		23-Jun-26		■ CFMF NC-NN x N4-N8																											
385		X4770	Blocking / Backing NC-NN x N4-N8	23-Jun-26		30-Jun-26		■ Blocking / Backing NC-NN x N4-N8																											
386		X4780	Drywall /Finish NC-NN x N4-N8	30-Jun-26		15-Jul-26		■ Drywall /Finish NC-NN x N4-N8																											
387		X4790	CFMF Hard Ceilings / Soffits NC-NN x N4-N8	16-Jul-26		28-Jul-26		■ CFMF Hard Ceilings / Soffits NC-NN x N4-N8																											
388		Main Level Addition Sou...	Main Level Addition South 2A Rough (A101.B)	13-Apr-26	A	07-Aug-26		■ Main Level Addition South 2A Rough (A101.B)																											
389		X4810	CMU Masonry NC-NN x N4-N8	13-Apr-26	A	13-May-26	A	■ CMU Masonry NC-NN x N4-N8																											
390		X4800	Install Door Frames NC-NN x N4-N8	13-Apr-26	A	15-May-26	A	■ Install Door Frames NC-NN x N4-N8																											
391		X4820	CFMF NC-NN x N4-N8	23-Jun-26		10-Jul-26		■ CFMF NC-NN x N4-N8																											
392		X4830	Blocking / Backing NC-NN x N4-N8	01-Jul-26		10-Jul-26		■ Blocking / Backing NC-NN x N4-N8																											
393		X4840	Drywall /Finish NC-NN x N4-N8	10-Jul-26		24-Jul-26		■ Drywall /Finish NC-NN x N4-N8																											
394		X4850	CFMF Hard Ceilings / Soffits NC-NN x N4-N8	28-Jul-26		07-Aug-26		■ CFMF Hard Ceilings / Soffits NC-NN x N4-N8																											
395		X4860	Interior R.I. Complete			07-Aug-26		◆ Interior R.I. Complete																											
396		Interior Finish	Interior Finish	21-Apr-26	A	20-Nov-26		■ Interior Finish																											
397		MEP T.O	MEP T.O	21-Apr-26	A	19-Nov-26		■ MEP T.O																											
398		Lower Level North 2A (...)	Lower Level North 2A (A-100.A)	06-Jul-26		21-Oct-26		■ Lower Level North 2A (A-100.A)																											
399		X5025	Set RTU's to Roof	06-Jul-26		13-Jul-26		■ Set RTU's to Roof																											
400		X5010	Trim out MEP's to Grid	30-Jul-26		12-Aug-26		■ Trim out MEP's to Grid																											
401		X5040	Mechanical Start-up / Functional Testing	13-Aug-26		19-Aug-26		■ Mechanical Start-up / Functional Testing																											
402		X5000	T.O. Wall Devices	21-Aug-26		28-Aug-26		■ T.O. Wall Devices																											
403		X5020	Plumbing Fixtures Restrooms	28-Aug-26		04-Sep-26		■ Plumbing Fixtures Restrooms																											
404		X5050	Test & Ballance	31-Aug-26		08-Sep-26		■ Test & Ballance																											
405		X5030	T.O. Plumbing to Millwork	21-Sep-26		28-Sep-26		■ T.O. Plumbing to Millwork																											
406		X5060	T.O Clocks	15-Oct-26		21-Oct-26		■ T.O Clocks																											
407		Lower Level South 2A (...)	Lower Level South 2A (A-100.B)	21-Apr-26	A	04-Nov-26		■ Lower Level South 2A (A-100.B)																											
408		X5130	Install Cooler / Freezer Insulated Panels	21-Apr-26	A	24-Apr-26	A	I Install Cooler / Freezer Insulated Panels																											



The Sherman School - Construction Schedule
Data Date: 01-Jun-26




	ID	Name	Start	Finish	2025														2026														2027														2028			
					J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M												
409		X5140	Install Kitchen Exhaust Hoods	21-Apr-26	A	24-Apr-26	A	I Install Kitchen Exhaust Hoods																																										
410		X5110	Generator Start-up	06-Jul-26		10-Jul-26		I Generator Start-up																																										
411		X5120	Generator Load Bank Testing	13-Jul-26		17-Jul-26		I Generator Load Bank Testing																																										
412		X5150	Plumbing Fixtures Restrooms	03-Aug-26		10-Aug-26		I Plumbing Fixtures Restrooms																																										
413		A2070	Install O.H Door Coil Grill in Kitchen	24-Aug-26		31-Aug-26		I Install O.H Door Coil Grill in Kitchen																																										
414		X5160	T.O. Wall Devices	28-Aug-26		04-Sep-26		I T.O. Wall Devices																																										
415		X5170	Trim out MEP's to Grid	31-Aug-26		15-Sep-26		I Trim out MEP's to Grid																																										
416		X5190	Mechanical Start-up / Functional Testing	15-Sep-26		22-Sep-26		I Mechanical Start-up / Functional Testing																																										
417		X5200	Test & Ballance	22-Sep-26		29-Sep-26		I Test & Ballance																																										
418		X5180	T.O. Plumbing to Millwork	30-Sep-26		07-Oct-26		I T.O. Plumbing to Millwork																																										
419		X5210	T.O Clocks	28-Oct-26		04-Nov-26		I T.O Clocks																																										
420		Main Level South 2A (...)	Main Level South 2A (A-101.B)	06-Jul-26		12-Nov-26		Main Level South 2A (A-101.B)																																										
421		X5335	Set RTU's to Roof	06-Jul-26		13-Jul-26		I Set RTU's to Roof																																										
422		X5220	Plumbing Fixtures Restrooms	28-Jul-26		04-Aug-26		I Plumbing Fixtures Restrooms																																										
423		X5230	Trim out MEP's to Grid	29-Sep-26		13-Oct-26		I Trim out MEP's to Grid																																										
424		X5240	T.O. Plumbing to Millwork	19-Oct-26		26-Oct-26		I T.O. Plumbing to Millwork																																										
425		X5250	Mechanical Start-up / Functional Testing	26-Oct-26		02-Nov-26		I Mechanical Start-up / Functional Testing																																										
426		X5270	T.O. Wall Devices	29-Oct-26		05-Nov-26		I T.O. Wall Devices																																										
427		X5260	Test & Ballance	02-Nov-26		09-Nov-26		I Test & Ballance																																										
428		X5280	T.O Clocks	05-Nov-26		12-Nov-26		I T.O Clocks																																										
429		Elevator	Elevator	16-Oct-26		10-Nov-26		Elevator																																										
430		X5070	MEP- F/A Terminations	16-Oct-26		26-Oct-26		I MEP- F/A Terminations																																										
431		X5080	Install Flooring	27-Oct-26		30-Oct-26		I Install Flooring																																										
432		X5090	Final Fit & Finish	02-Nov-26		05-Nov-26		I Final Fit & Finish																																										
433		X5100	Functional Testing	06-Nov-26		10-Nov-26		I Functional Testing																																										
434		Main Level North 2A (...)	Main Level North 2A (A-101.A)	11-Aug-26		19-Nov-26		Main Level North 2A (A-101.A)																																										
435		X5290	Plumbing Fixtures Restrooms	11-Aug-26		18-Aug-26		I Plumbing Fixtures Restrooms																																										
436		X5300	T.O. Plumbing to Millwork	18-Aug-26		25-Aug-26		I T.O. Plumbing to Millwork																																										
437		X5310	Trim out MEP's to Grid	15-Sep-26		29-Sep-26		I Trim out MEP's to Grid																																										
438		X5340	T.O. Wall Devices	22-Oct-26		29-Oct-26		I T.O. Wall Devices																																										
439		X5320	Mechanical Start-up / Functional Testing	02-Nov-26		09-Nov-26		I Mechanical Start-up / Functional Testing																																										
440		X5330	Test & Ballance	09-Nov-26		16-Nov-26		I Test & Ballance																																										
441		X5350	T.O Clocks	12-Nov-26		19-Nov-26		I T.O Clocks																																										
442		Main Level Addition So...	Main Level Addition South 2A (A-101.B)	13-Jul-26		19-Nov-26		Main Level Addition South 2A (A-101.B)																																										



The Sherman School - Construction Schedule
Data Date: 01-Jun-26



	ID	Name	Start	Finish																													
					2025							2026							2027							2028							
					J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O
443		X5365	Set RTU's to Roof	13-Jul-26	20-Jul-26															▮ Set RTU's to Roof													
444		X5360	Plumbing Fixtures Restrooms	18-Aug-26	25-Aug-26															▮ Plumbing Fixtures Restrooms													
445		X5410	T.O. Wall Devices	25-Sep-26	02-Oct-26															▮ T.O. Wall Devices													
446		X5370	Trim out MEP's to Grid	13-Oct-26	27-Oct-26															▮ Trim out MEP's to Grid													
447		X5380	Mechanical Start-up / Functional Testing	27-Oct-26	03-Nov-26															▮ Mechanical Start-up / Functional Testing													
448		X5390	T.O. Plumbing to Millwork	06-Nov-26	13-Nov-26															▮ T.O. Plumbing to Millwork													
449		X5400	Test & Ballance	09-Nov-26	16-Nov-26															▮ Test & Ballance													
450		X5420	T.O Clocks	12-Nov-26	19-Nov-26															▮ T.O Clocks													
451		Lower Level North 2A Fi...	Lower Level North 2A Finish (A100.A)	19-Jun-26	06-Nov-26															▮ Lower Level North 2A Finish (A100.A)													
452		X5430	Block Fill Prime / Paint CMU	19-Jun-26	29-Jun-26															▮ Block Fill Prime / Paint CMU													
453		X5440	Hard Tile Restrooms	13-Jul-26	31-Jul-26															▮ Hard Tile Restrooms													
454		X5460	ACT Ceiling Grid	20-Jul-26	29-Jul-26															▮ ACT Ceiling Grid													
455		X5465	Floor Leveling	29-Jul-26	05-Aug-26															▮ Floor Leveling													
456		X5450	Prime / Paint Drywall	07-Aug-26	21-Aug-26															▮ Prime / Paint Drywall													
457		X5480	LVT Tile Installations	20-Aug-26	26-Aug-26															▮ LVT Tile Installations													
458		X5510	Doors & Hardware	27-Aug-26	08-Sep-26															▮ Doors & Hardware													
459		X5500	Finish Drywall Soffits & Install Acoustical Ceiling Tiles	31-Aug-26	08-Sep-26															▮ Finish Drywall Soffits & Install Acoustical Ceiling Tiles													
460		X5490	Install Toilet Partitions	04-Sep-26	16-Sep-26															▮ Install Toilet Partitions													
461		X5530	Install Stair Treads	08-Sep-26	17-Sep-26															▮ Install Stair Treads													
462		X5475	Close Ceilings	08-Sep-26	16-Sep-26															▮ Close Ceilings													
463		X5470	Classroom Millwork / Casework	14-Sep-26	21-Sep-26															▮ Classroom Millwork / Casework													
464		X5520	Install Lockers	05-Oct-26	14-Oct-26															▮ Install Lockers													
465		X5540	Finish Painting	06-Oct-26	14-Oct-26															▮ Finish Painting													
466		X5550	Install Visual Display Boards	15-Oct-26	22-Oct-26															▮ Install Visual Display Boards													
467		X5560	Signage	15-Oct-26	21-Oct-26															▮ Signage													
468		X5580	Electronic Display Boards	15-Oct-26	21-Oct-26															▮ Electronic Display Boards													
469		X5590	Install Carpet	15-Oct-26	23-Oct-26															▮ Install Carpet													
470		X5600	"HEPA" Cleaning	26-Oct-26	30-Oct-26															▮ "HEPA" Cleaning													
471		X5610	NCG Completion List	02-Nov-26	06-Nov-26															▮ NCG Completion List													
472		Lower Level South 2A Fi...	Lower Level South 2A Finish (A100.B)	29-Jun-26	19-Nov-26															▮ Lower Level South 2A Finish (A100.B)													
473		X5620	Block Fill Prime / Paint CMU	29-Jun-26	08-Jul-26															▮ Block Fill Prime / Paint CMU													
474		X5630	Hard Tile Restrooms	08-Jul-26	22-Jul-26															▮ Hard Tile Restrooms													
475		X5640	Prime / Paint Drywall	08-Jul-26	22-Jul-26															▮ Prime / Paint Drywall													
476		X5660	Install Toilet Partitions	22-Jul-26	31-Jul-26															▮ Install Toilet Partitions													

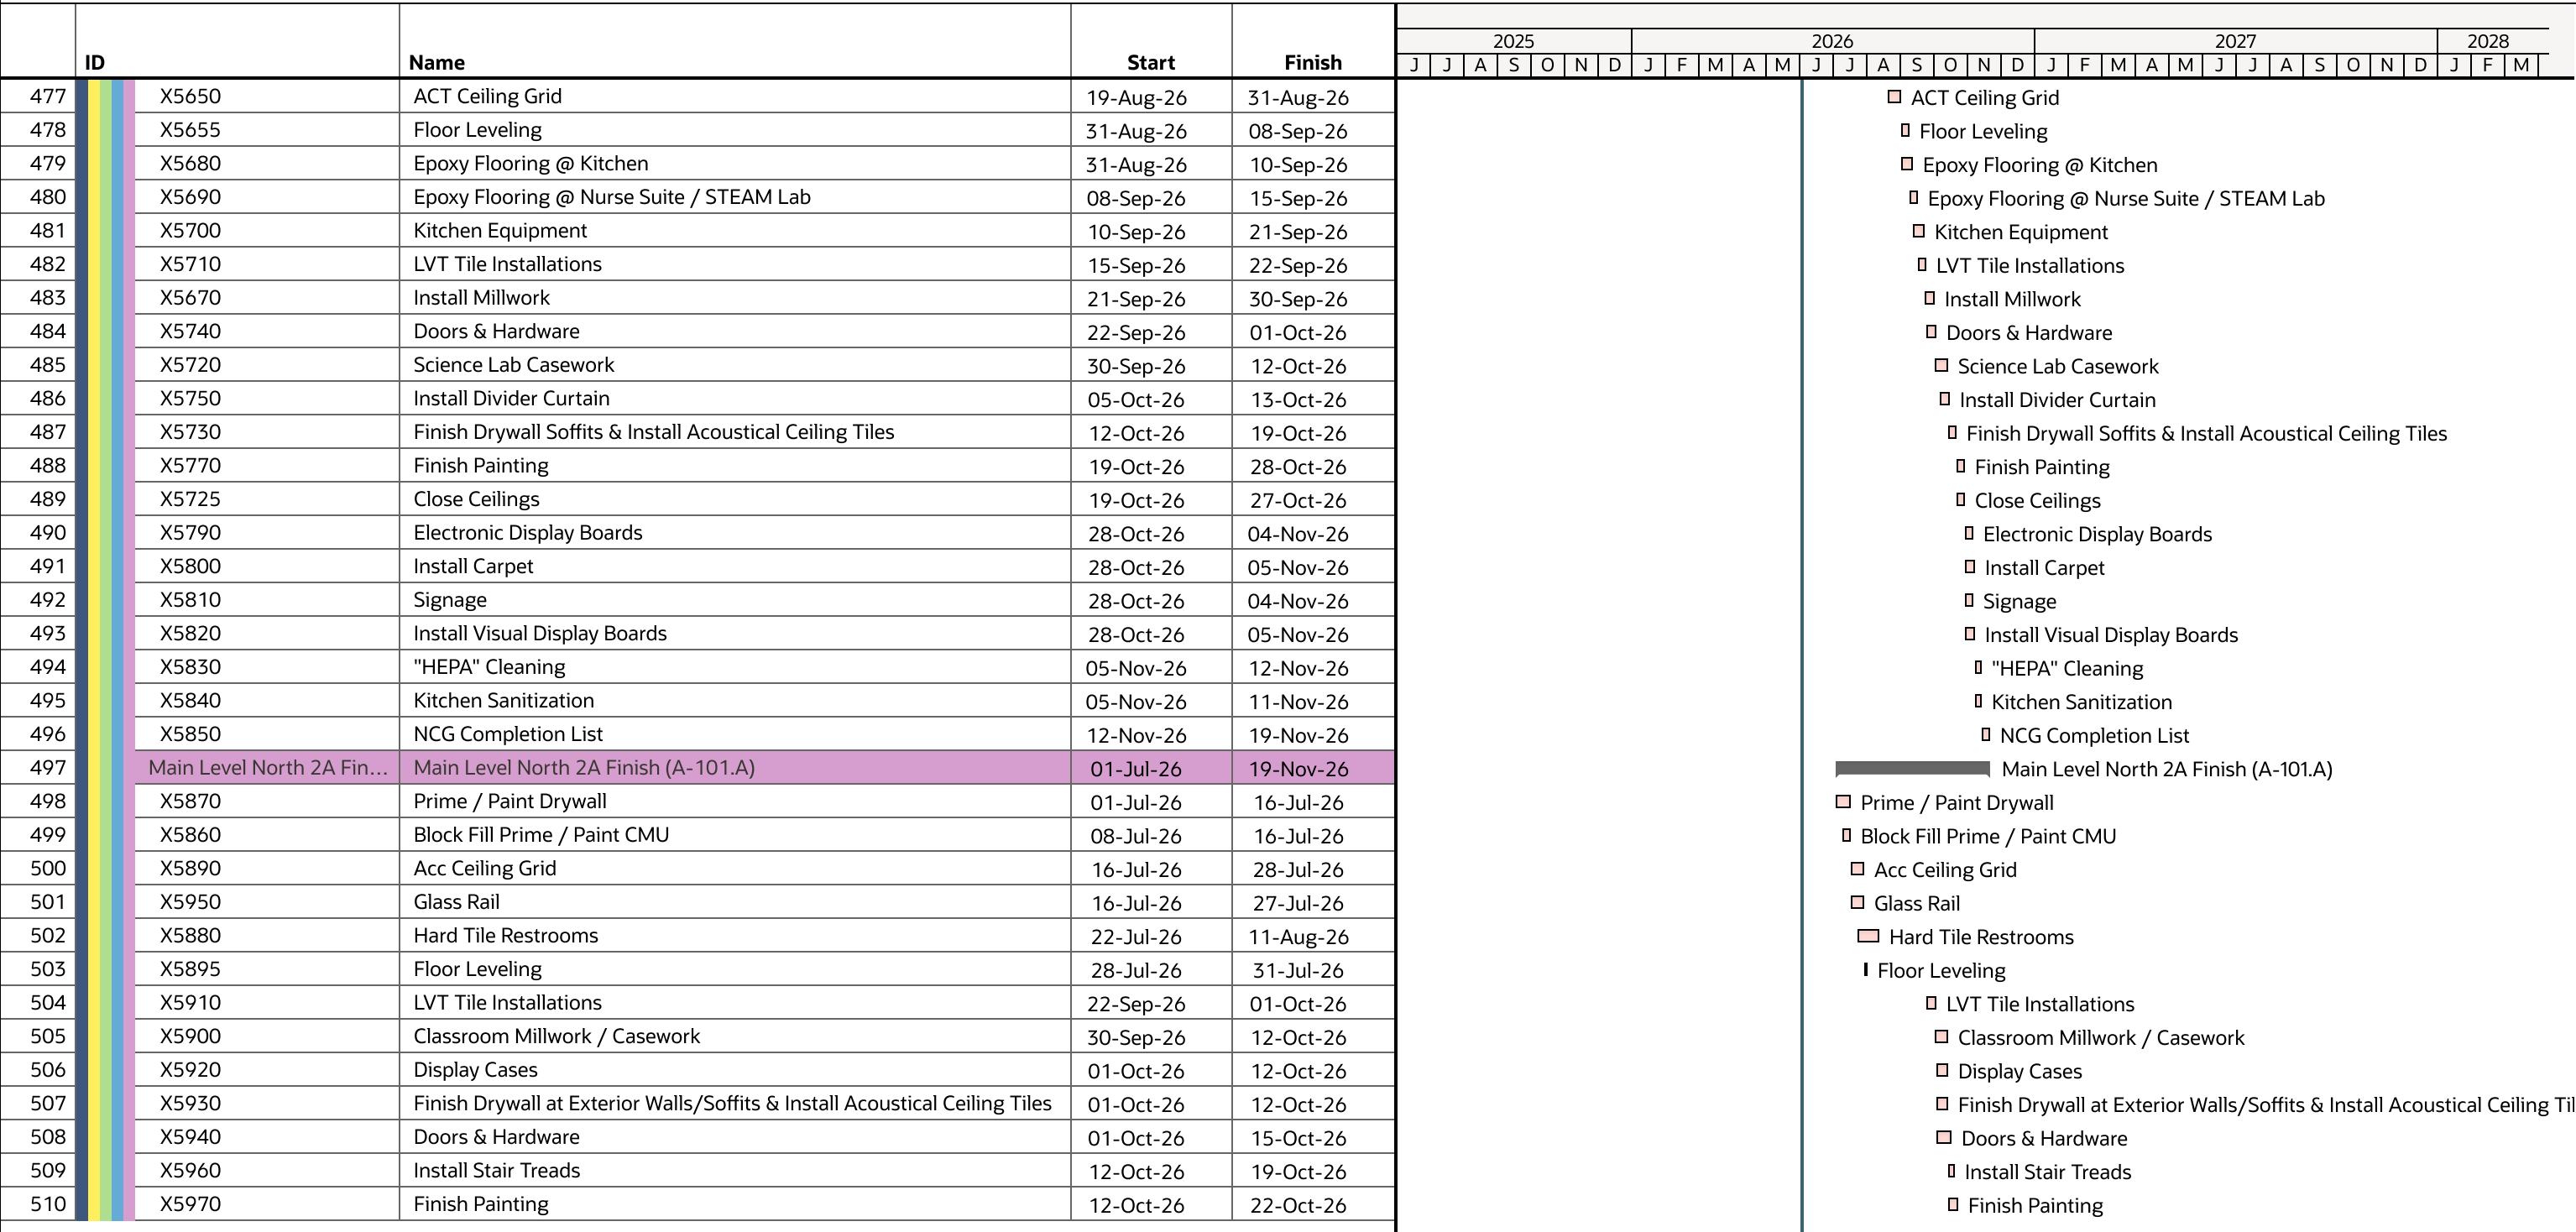




The Sherman School - Construction Schedule
Data Date: 01-Jun-26



	ID	Name	Start	Finish																													
					2025							2026							2027							2028							
					J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O
511		X5915	Close Ceilings	12-Oct-26	20-Oct-26															<													

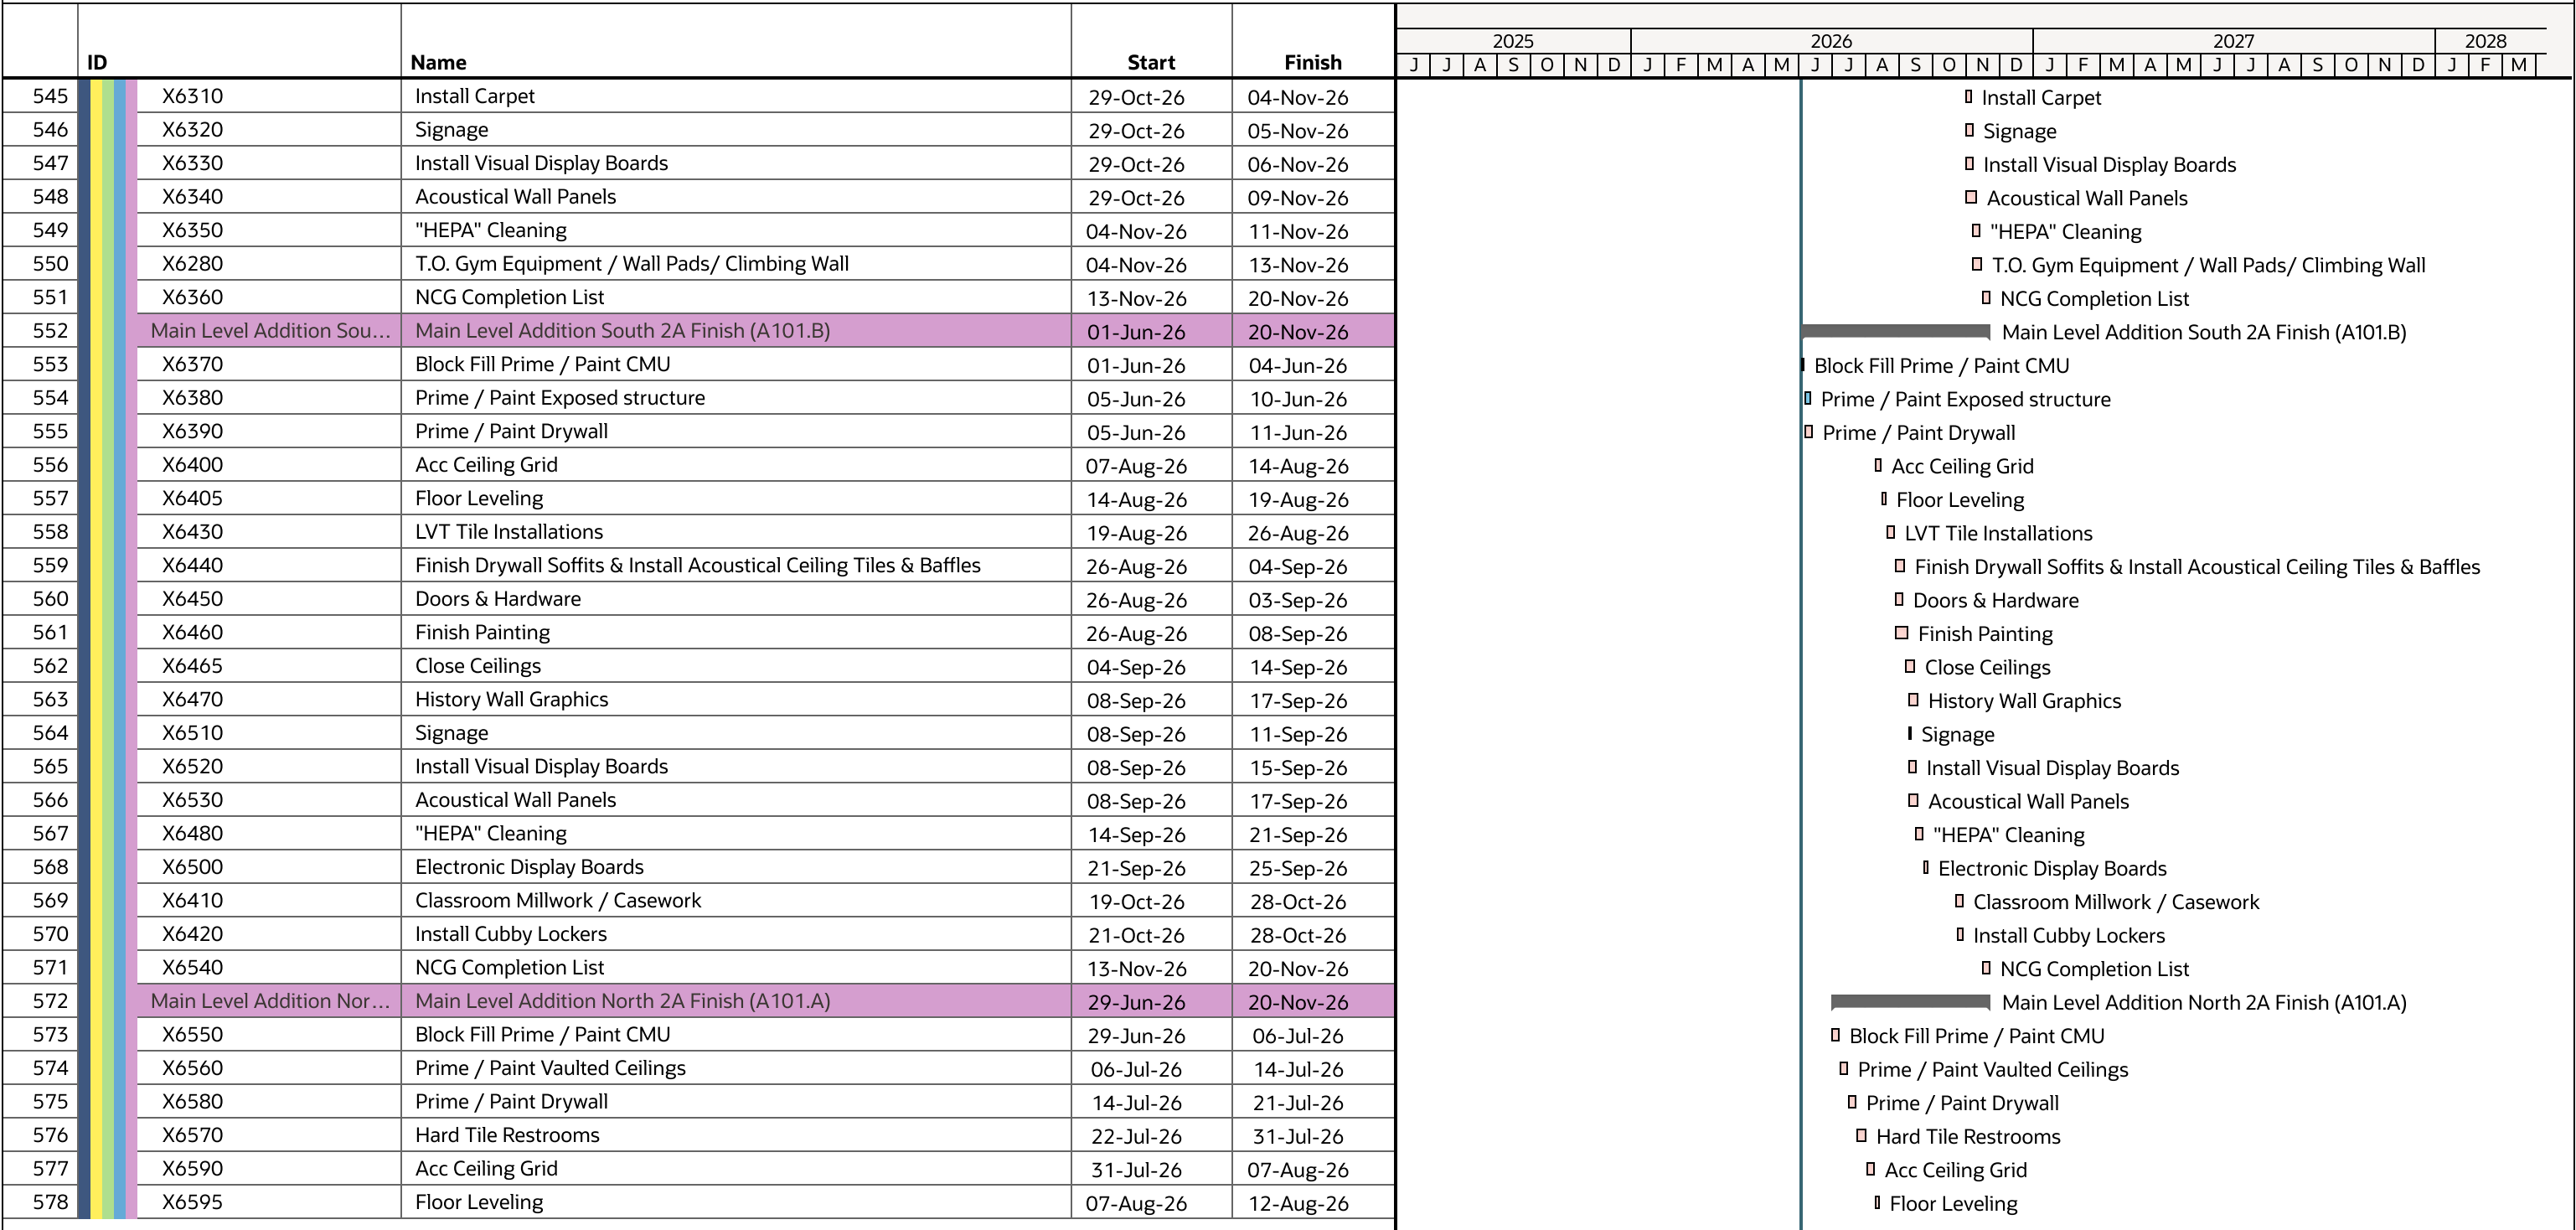



Project ID: 24-014
Prepared By: Ben Chasse
06-Jun-26 10:25 a.m.
01-Jun-26

Page: 18 of 19

Current

Progress

Critical

Milestones

Summary



The Sherman School - Construction Schedule
Data Date: 01-Jun-26



	ID	Name	Start	Finish																								
					2025							2026							2027							2028		
					J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M
613	Z1020	As-Built Document Submission	16-Dec-26	23-Dec-26																								
614	Z1010	Owner Training	16-Dec-26	22-Jan-27																								
615	Z1030	Attic stock	23-Dec-26	08-Jan-27																								
616	Z1000	Submission of Close out Manuals	23-Dec-26	05-Feb-27																								
617	A2030	Phase 2A Closeout Complete		05-Feb-27																								
618	Phase 2B	Phase 2B	07-Jul-27	02-Sep-27																								

- As-Built Document Submission
- Owner Training
- Attic stock
- Submission of Close out Manuals
- Phase 2A Closeout Complete
- Phase 2B
